Waterline Controls®

ETL LISTED - INTERTEK - C US

SENSOR APPROVAL SHEET

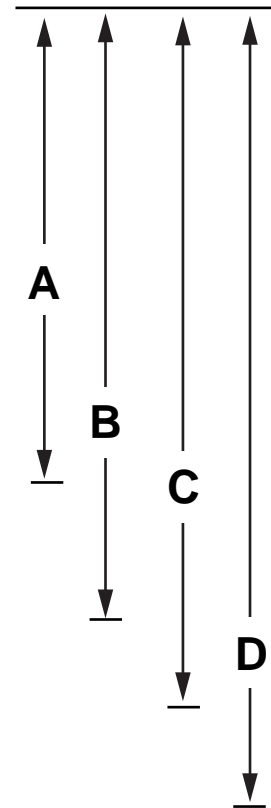|	
CUSTOMER	
PO#	
SO#	
SHIP DATE	
QUANTITY	
WIRE LENGTH (Ft.)	
CONTINUOUS	

OPTIONS
- Temperature Alarm activations
- Temp. cut-out at 40° per NFPA 22 16.1.2.2
- Wire length (min. 50 ft. - 350 ft. max.)
- Operates value
- Audible Alarm

3" Slip Plug (PVC)

3" Slip Fitting

WLC Controls

Reference - BLACK
Low Alarm - BROWN
Fill Level ON - WHITE
Fill Level OFF - RED
High Alarm - GREEN

All Sensors are stainless steel

HIGH ALARM Green

FILL OFF Red

FILL ON White

REFERENCE Black

LOW ALARM Brown

All ends: 1/4 - 20 Threaded

A
B
C
D

Dimensions should be calculated from the top of the tank or riser down to the required alarm level(s) in inches. Be sure to take into account any riser pipes or manway risers.

Waterline Controls
P.O. Box 12544
Scottsdale, Arizona 85260
Toll Free: 888-905-1892
info@waterlinecontrols.com
www.waterlinecontrols.com

SENSOR			LENGTH
Green	HIGH	A	
Red	OFF (Fill)	B	
White	ON (Fill)	C	
Brown	LOW	D	
Black	Same length as longest Rod		
Temp-Optional			

Name:

Company:

Signature:

Date:

Signature is required to release product to production
