
3030 Sensor Approval
Simplex Fill

CUSTOMER
PO#
SO#
REQUESTED SHIP DATE
QUANTITY
CABLE LENGTH (ft.)

Standard Cable length is 50 ft.
Available in 50ft increments up to 350 ft.
Over 350 ft. please call

All rods are 304L stainless steel with 1/4-20 threaded ends.
Sensor rods can be extended using an Extension Rod kit accessory.
Sensor rods & wires are Intrinsically safe with circuit limited signals.

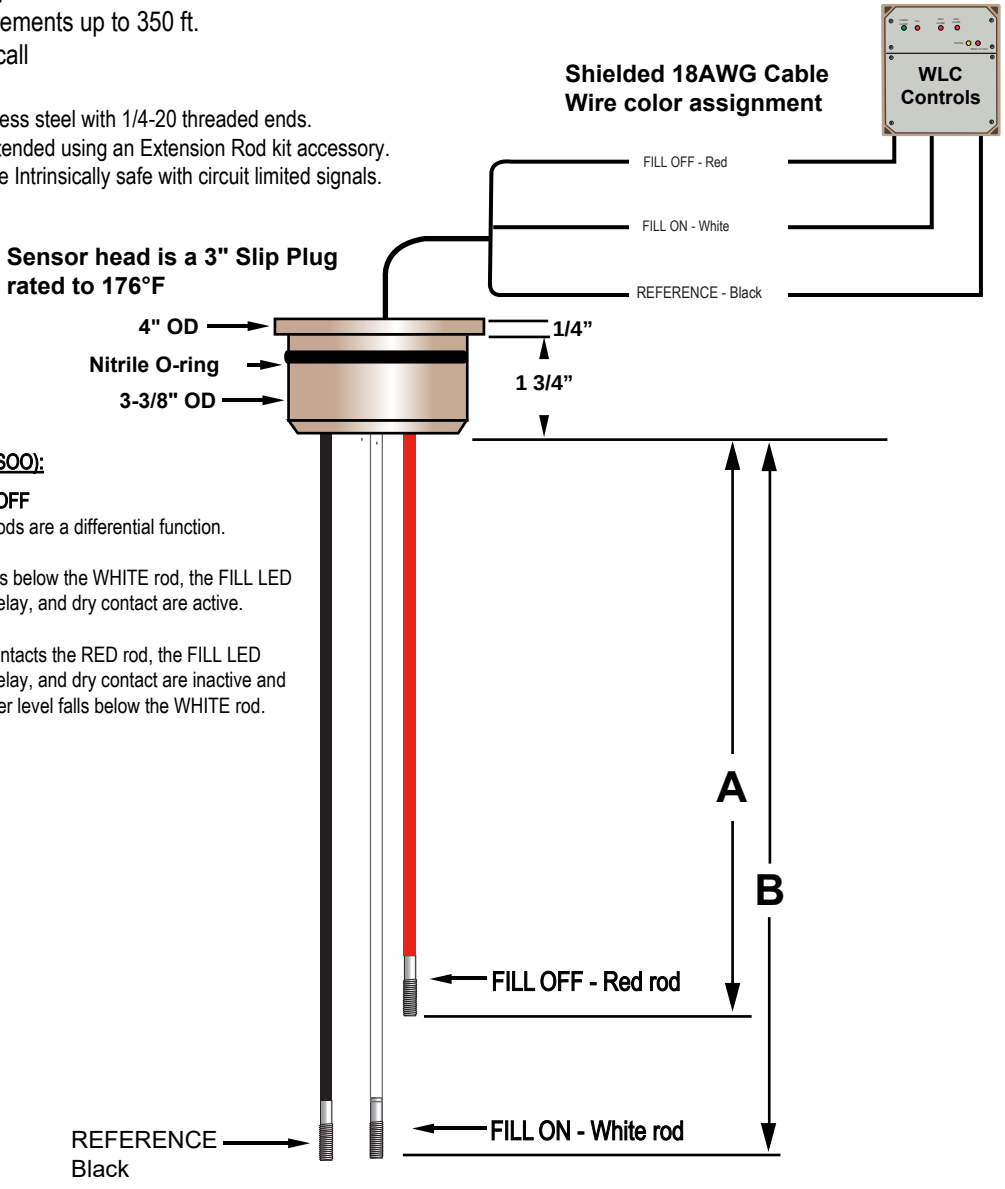

Sequence of Operation (SOO):

FUNCTION 1: FILL ON/OFF
The RED AND WHITE rods are a differential function.

When the water level falls below the WHITE rod, the FILL LED status indicator, power relay, and dry contact are active.

When the water level contacts the RED rod, the FILL LED status indicator, power relay, and dry contact are inactive and remain inactive until water level falls below the WHITE rod.

Sensor rods & wires are Intrinsically safe with circuit limited signals

Waterline Controls
P.O. Box 12544
Scottsdale, Arizona 85267
Phone: 480-905-1892
info@waterlinecontrols.com
www.waterlinecontrols.com

Custom rod length requests should be measured from where the bottom of the sensor cup will be seated after mounting, down to the required function or alarm level(s) in inches. Be sure to take into account any riser pipes or man-way risers

Fill Custom in as needed

PROBES		LENGTHS (Inches)		
		Standard		Custom
Red	FILL OFF	A	15-1/2"	
White	FILL ON	B	17"	
Black	REFERENCE	B	Same as longest rod	

Name:

Company:

Signature:

Date:

Signature is required to release product to production

© SDI 2026
